



**BOARD OF EDUCATION  
SCHOOL DISTRICT NO. 50  
HAIDA GWAII**

107 Third Avenue, PO Box 69  
Village of Daajing Giids, BC V0T 1S0  
Tel: (250) 559-8471 Fax: (250) 559-8849  
[www.sd50.bc.ca](http://www.sd50.bc.ca)

## **Gudangaay Tlaats'гаа Naay Project Update**

July 13, 2023

Dear staff, students and all community members, here is a brief update of the Masset schools project and where we are at for July 13, 2023. The project continues to move forward and now that Phase 3 has started more work progress continues.

Below is a short list of progress items for the month of June:


- 119 & 120 + Corridor Foundation formwork stripped.
- Foundation damp proof and drainage board installed.
- Rigid insulation installed on foundation.
- Washroom 133 rain water leader (RWL) tied into new catch basin/drainage under 119 & 120.
- Backfill & compaction of 119 & 120 exterior foundation walls completed.
- Interior foundation back fill and compaction in progress (IP) – 98%.
- Heating lines in Library removed and new system hangers' installation complete.
- New temporary supports added to existing overhead mechanical and electrical in new corridor off 120 to facilitate back fill and future framing.
- Pour 119 & 120 footings and walls.
- Strip some forms to allow remaining foundation wall and footing formwork, and concrete pour.
- Complete all 119 & 120 foundation concrete.
- Concrete placed for new footing in room 108.
- New Assistant Site Superintendent arrived.

We will continue to keep everyone updated on a regular basis, if you have any questions, please reach out to Lao Peerless or Kevin Black.


Manager of Operations:  
Secretary-Treasurer:

Lao Peerless  
Kevin Black


[lpeerless@sd50.bc.ca](mailto:lpeerless@sd50.bc.ca)  
[kblack@sd50.bc.ca](mailto:kblack@sd50.bc.ca)

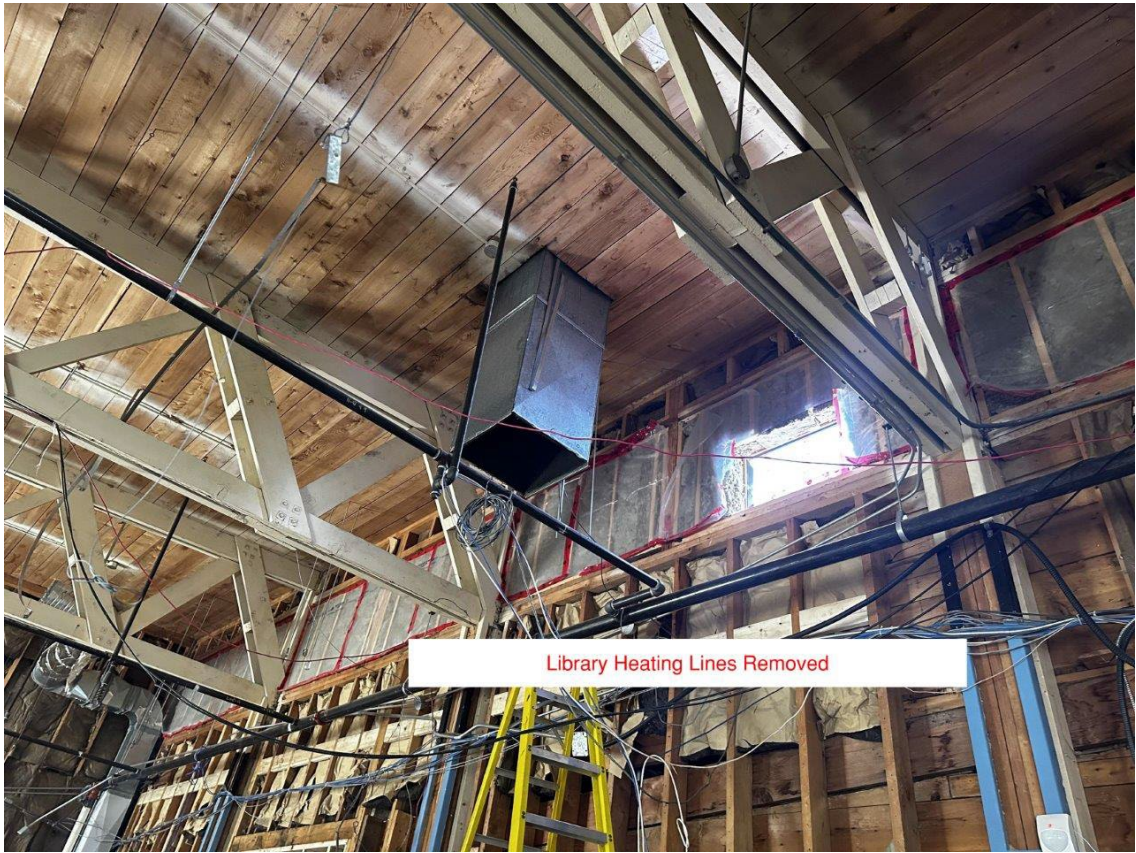

Library Heating Lines Removed

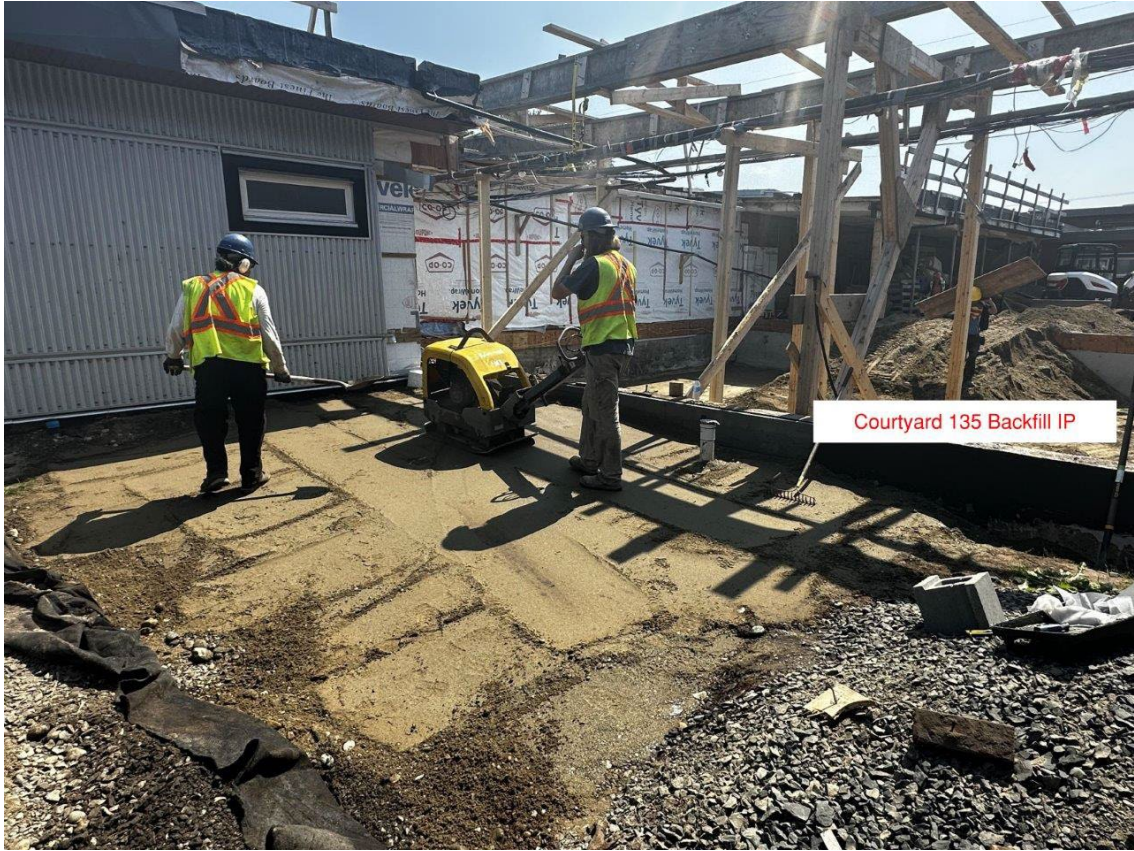

Courtyard 135 Backfill IP

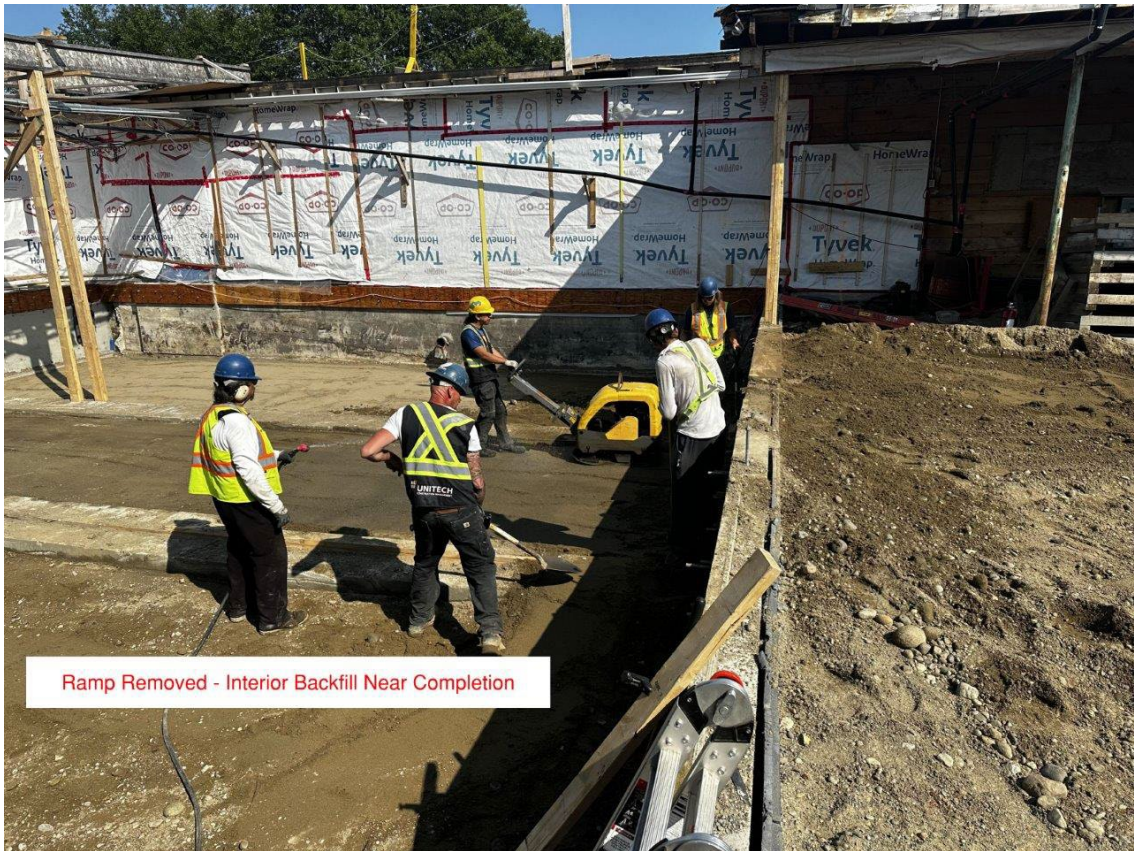

Ramp Removed - Interior Backfill Near Completion

Re-setting Concrete Pump Hose





East Library Wall Plywood Edge Blocking IP.
